

Paradise Regional Recreation Center

Monthly Construction Project Update

Presented By:

Mike Harris

Director, District Property Management

Paradise Regional Recreation Center



Timeline

- **September 2025** – Demolition Phase (~90 Day Duration)
- **November 2025** – Construction Phase (~450 Day Duration)
- **Spring 2027** – Projected Grand Opening (~540 Day Duration)

Communications & Updates


- A dedicated web page for the Paradise Regional Recreation Center construction project featuring project updates, photos & videos is available now.
- [Click here to be directed to the Paradise Recreation Center Construction Page.](#)

Paradise Regional Recreation Center

Project Updates

Ongoing tasks:

- Interior framing and walls are in progress.
- Plumbing rough in work continues throughout the main building.
- Electrical rough in work is ongoing, including setting floor boxes and additional main building installations.
- Metal deck installation and steel punch out activities are underway.
- HVAC installation and sprinkler coordination continue in different building areas.
- Masonry tasks and general construction support activities continue day to day.
- Structural modifications such as adding tubing to I beams and pavilion modifications are progressing.

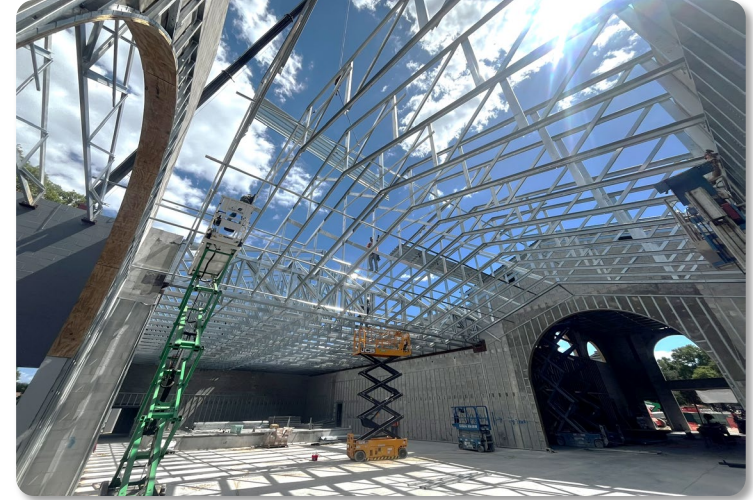

Thank you!
