

# Paradise Regional Recreation Center

## *Monthly Construction Project Update*

**Presented By:**

**Mike Harris**

**Director, District Property Management**

# Paradise Regional Recreation Center



## Timeline

- **September 2025** – Demolition Phase (~90 Day Duration)
- **November 2025** – Construction Phase (~450 Day Duration)
- **Spring 2027** – Projected Grand Opening (~540 Day Duration)

## Communications & Updates

- A dedicated web page for the Paradise Regional Recreation Center construction project featuring project updates, photos & videos is available now.
- [Click here to be directed to the Paradise Recreation Center Construction Page.](#)

# Paradise Regional Recreation Center


## Project Updates

### Completed tasks:

- Framing of interior areas and front entry
- Integration of fire sprinkler system
- Installation of electrical conduit for HVAC controls
- Rough-ins and drainpipe insulation in the main building
- Application of stucco on the pool building
- Installation of TPO roofing
- Flashing on the main building

### Ongoing tasks:

- Exterior fascia installation is underway
- Ductwork installation is ongoing
- Storm pipe installation continues
- Installation of coping and tiles is in progress

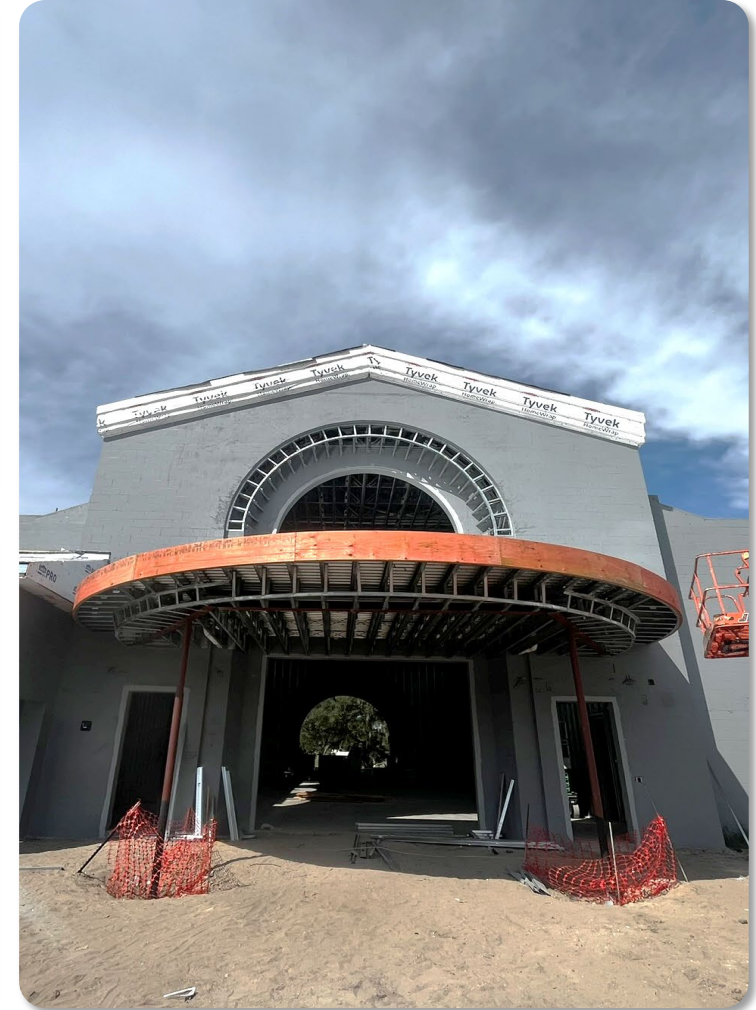

*Thank you!*
